January 1, 2008

Visit our showroom at: Classic Log Homes, Inc. 845 Hwy. 73 South Wisc. Rapids, WI 54494

8" Stack Ht. 9"-10" Average Thickness 78 x 36 Rustic D-Style Log Package Estimate Approximate est. for the Harrison with attached garage

www.classicloghomes.biz

715-887-2550

Authentic Hand-Peeled in Natural / Rustic Quality products at Wholesale prices!

This estimate is for a 78ft x 36ft log cabin in authentic hand-peeled 8 inch stack D-style logs with 10ft high full log walls and log sided gable ends. It includes 2 tie logs overhead on the main level and a log ridge beam. It also includes the gasketing and hardware. This log package is totally modifiable to fit your individual needs. Please call if you have any questions.



Qty. L/F	\$]	Ln/ Ft	\$ Each	Description	(Options	Total
3,720	\$	4.50		8" stack rough-sawn three sides, D-style white pine wall logs, traditional butt and			\$ 16,740.00
				pass in natural- rustic.			
5,292	\$	2.25		Matching 3" x 8" log siding figured for the outside of the gable walls (interior			\$ 11,907.68
				gables included in options list) Note: you can also use full logs for the gables.			
440	\$	2.25		3" x 8" log siding figured for the outside of the dormer walls for a 16' shed style	\$	990.00	
				dormer. Note: This optional dormer estimate is not in the total below.			
10			\$ 18.00	Handleing charge for Natural Tails 150 needed for 10 corners	\$	2,700.00	
				(double quantity for the saddle notch) Note: This option is not included in total.			
5,292	\$	1.06		Matching 2" x 8" ruff sawn boards figured for the interior gable walls	\$	11,907.68	
24	\$	8.40		10" stack double round flat top & bottom log beam to support floor joist	\$	201.60	
160	\$	9.60		2-Log cross ties, 9" top diameter	\$	1,536.00	
560	\$	6.40		Optional log floor joist, flat one side 10" top diameter	\$	3,584.00	
30	\$	3.68		8' post, 8" top diameter	\$	110.40	
36	\$	4.80		Log ridge beam	\$	172.80	
9,012	\$	0.50		1/4" x 1/4" bead of conceal log caulk inside and out for the basic package	\$	4,506.15	
9,012	\$	0.60		Foam Gasketing and Fastwing Log Screws	\$	5,407.38	
17			\$172.50	Log stairs (\$172.50 per tread includes split log treads and 2 choices of log stringers)	\$	2,932.50	
8			\$ 24.38	*Cedar log post 6" diameter x 48" high with pre notching and drilling (figure one post per 8' section of rail plus one for the end)	\$	195.04	
20	\$	18.00		*Pre-assembled northern white cedar log railings for horizontal areas.	\$	360.00	
16	\$	21.75		*Pre-assembled northern white cedar log railings for stairs.	\$	348.00	
- 10	-	21170		*Total for interior log railings: \$694.40	Ψ.	2.0.00	
				*For the exterior railings you may need 7-7' sections and 5-48" posts	\$	949.02	
36	\$	140.00		36FT log porch to cover an 8ft wide deck with log posts 8ft on center and a single log beam with log rafters 4ft on center and covered with 2x8 tongue and groove.	\$	5,040.00	
2,059	\$	1.78	/ sqft	\$1.78 sq.ft. for 2" x 8" Tongue and groove pine floor for the loft	\$	3,665.38	
			- 1	Total for all options		40,915.94	
	_			e size listed, * log railings are not plan specific, for an exact price please submit a			
				f materials. We would be happy to help please give us a call.			
				d in central Wisconsin area, and includes a piggy back fork lift and unloading the ther area please call. Note: your order may require more loads.			
							\$ 28,647.68
All orders require a deposit of 50%. The balance will be due before shipment. Final payments payable by cashers							\$ 1,575.62
check unless paid in advance. Deposits are non-refundable. This is an estimate for log materials only and does not							\$ 450.00
		incl	ude: Iabor,	foundation, sub-floor, roof, interior walls, windows, doors, etc.		Estimate	¢ 20 (72 20
						i otai Due	\$ 30,673.30

Basic log package before tax and shipping	Sub-total	\$ 28,647.68
Total for all options	Options total	\$ 40,915.94
Complete log package estimate before tax and shipping	Total	\$ 69,563.62


Enter dimen	sion information	on he	ere		
	Dimensions				
ENTER	Width	78			
ENTER	Length		36		
ENTED	Additional		20		
ENTER	full log walls				
ENTER	Wall Height		10		
# courses	Main sqft		2,808		
	total				
15	Loft sqft total		1,872		
# corners	Total sqft		4,680		
10	sub-total	\$	28,647.68		
wall footage	option total	\$	40,915.94		
	total total	\$	69,563.62		
	nat. tails	\$	2,700.00		
	total w/tails	\$	72,263.62		
			·		



Inside view with wane on the corners



Matching 3" x 8" log siding

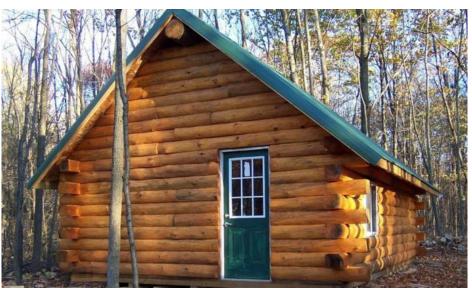

Natural hand-peeled D-Logs
