

Visit our showroom at:
 Classic Log Homes, Inc.
 845 Hwy. 73 South
 Wisc. Rapids, WI 54494
 715-887-2550

January 1, 2008

8" Stack Ht. 9"-10" Average Thickness
32 x 44 Rustic D-Style Log Package Estimate
Main Floor 1408 /sqft, Loft 939 /sqft, Total sqft 2347



www.classicloghomes.biz

Authentic Hand-Peeled in Natural / Rustic
 Quality products at Wholesale prices!

This estimate is for a 32ft x 44ft log cabin in authentic hand-peeled 8 inch stack D-style logs with 10ft high full log walls and log sided gable ends. It includes 2 tie logs overhead on the main level and a log ridge beam. It also includes the gasketing and hardware. This log package is totally modifiable to fit your individual needs. Please call if you have any questions.

Qty. L/F	\$ Ln/ Ft	\$ Each	Description	Options	Total
2,730	\$ 4.50		8" stack rough-sawn three sides, D-style white pine wall logs, traditional butt and pass in natural- rustic.		\$ 12,285.00
883	\$ 2.25		Matching 3" x 8" log siding figured for the outside of the gable walls (interior gables included in options list) Note: you can also use full logs for the gables.		\$ 1,987.20
440	\$ 2.25		3" x 8" log siding figured for the outside of the dormer walls for a 16' shed style dormer. Note: This optional dormer estimate is not in the total below.	\$ 990.00	
4		\$ 18.00	Handleing charge for Natural Tails 60 needed for 4 corners (double quantity for the saddle notch) Note: This option is not included in total.	\$ 1,080.00	
883	\$ 1.06		Matching 2" x 8" ruff sawn boards figured for the interior gable walls	\$ 1,987.20	
30	\$ 8.40		10" stack double round flat top & bottom log beam to support floor joist	\$ 252.00	
68	\$ 9.60		2-Log cross ties, 9" top diameter	\$ 652.80	
306	\$ 6.40		Optional log floor joist, flat one side 10" top diameter	\$ 1,958.40	
30	\$ 3.68		8' post, 8" top diameter	\$ 110.40	
44	\$ 4.80		Log ridge beam	\$ 211.20	
3,613	\$ 0.50		1/4" x 1/4" bead of conceal log caulk inside and out for the basic package	\$ 1,806.60	
3,613	\$ 0.60		Foam Gasketing and Fastwing Log Screws	\$ 2,167.92	
17		\$172.50	Log stairs (\$172.50 per tread includes split log treads and 2 choices of log stringers)	\$ 2,932.50	
8		\$ 24.38	*Cedar log post 6" diameter x 48" high with pre notching and drilling (figure one post per 8' section of rail plus one for the end)	\$ 195.04	
20	\$ 18.00		*Pre-assembled northern white cedar log railings for horizontal areas.	\$ 360.00	
16	\$ 21.75		*Pre-assembled northern white cedar log railings for stairs.	\$ 348.00	
			*Total for interior log railings: \$694.40		
			*For the exterior railings you may need 7-7' sections and 5-48" posts	\$ 949.02	
44	\$ 140.00		44FT log porch to cover an 8ft wide deck with log posts 8ft on center and a single log beam with log rafters 4ft on center and covered with 2x8 tongue and groove.	\$ 6,160.00	
1,033	\$ 1.78 / sqft		\$1.78 sq.ft. for 2" x 8" Tongue and groove pine floor for the loft	\$ 1,838.56	
			Total for all options	\$ 21,929.64	
This is a ballpark estimate for the size listed, * log railings are not plan specific, for an exact price please submit a full set of plans or a detailed list of materials. We would be happy to help please give us a call.					
Shipping is estimated for one load in central Wisconsin area, and includes a piggy back fork lift and unloading the truck. If you need a quote for another area please call. Note: your order may require more loads.					
All orders require a deposit of 50%. The balance will be due before shipment. Final payments payable by cashers check unless paid in advance. Deposits are non-refundable. This is an estimate for log materials only and does not include: labor, foundation, sub-floor, roof, interior walls, windows, doors, etc.				Sub-Total	\$ 14,272.20
				5.5% WI Tax	\$ 784.97
				Shipping Estimate	\$ 450.00
				Total Due	\$ 15,507.17

Basic log package before tax and shipping	Sub-total	\$ 14,272.20
Total for all options	Options total	\$ 21,929.64
Complete log package estimate before tax and shipping	Total	\$ 36,201.84

Note: 5.5% Sales Tax is only for Wisconsin Residents

Enter dimension information here

Dimensions		
ENTER	Width	32
ENTER	Length	44
ENTER	Additional full log walls	30
ENTER	Wall Height	10
# courses	Main sqft total	1,408
15	Loft sqft total	939
# corners	Total sqft	2,347
4	sub-total	\$ 14,272.20
wall footage	option total	\$ 21,929.64
182	total total	\$ 36,201.84
	nat. tails	\$ 1,080.00
	total w/tails	\$ 37,281.84




Inside view with wane on the corners



Matching 3" x 8" log siding

Square footage is based on the loft size being 2/3 the main floor.

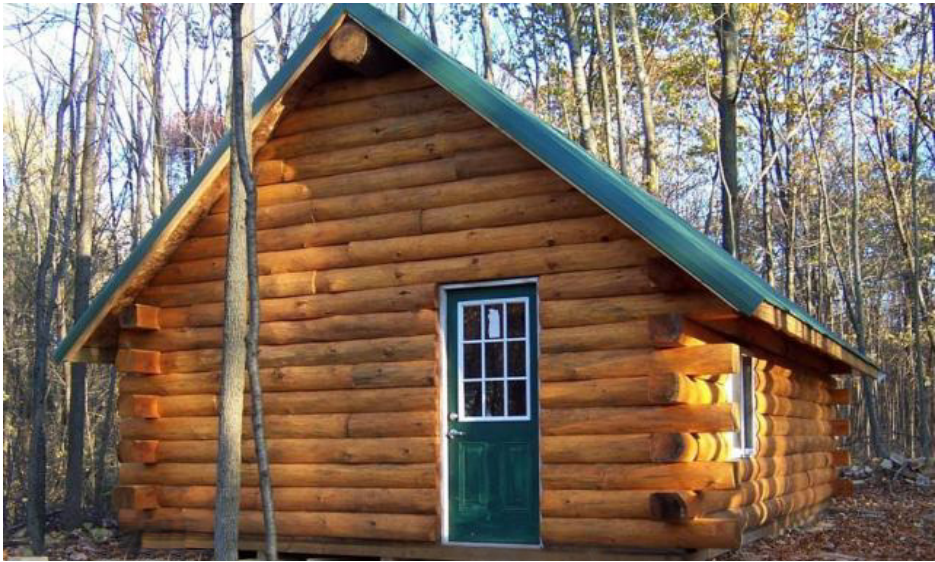

Natural hand-peeled D-Logs
