

Visit our showroom at:
Classic Log Homes, Inc.
 845 Hwy. 73 South
 Wisc. Rapids, WI 54494
 715-887-2550
www.classicloghomes.biz

January 1, 2008

8" Stack Ht. 9"-10" Average Thickness
36 x 64 Rustic D-Style Log Package Estimate
 Approximate est. for the Cape Scott



Authentic Hand-Peeled in Natural / Rustic
 Quality products at Wholesale prices!



This estimate is for a 36ft x 64ft log cabin in authentic hand-peeled 8 inch stack D-style logs with 10ft high full log walls and log sided gable ends. It includes 2 tie logs overhead on the main level and a log ridge beam. It also includes the gasketing and hardware. This log package is totally modifiable to fit your individual needs. Please call if you have any questions.

Qty. L/F	\$ Ln/ Ft	\$ Each	Description	Options	Total
3,900	\$ 4.50		8" stack rough-sawn three sides, D-style white pine wall logs, traditional butt and pass in natural- rustic.		\$ 17,550.00
1,118	\$ 2.25		Matching 3" x 8" log siding figured for the outside of the gable walls (interior gables included in options list) Note: you can also use full logs for the gables.		\$ 2,515.05
440	\$ 2.25		3" x 8" log siding figured for the outside of the dormer walls for a 16' shed style dormer. Note: This optional dormer estimate is not in the total below.	\$ 990.00	
10		\$ 18.00	Handleing charge for Natural Tails 150 needed for 10 corners (double quantity for the saddle notch) Note: This option is not included in total.	\$ 2,700.00	
1,118	\$ 1.06		Matching 2" x 8" ruff sawn boards figured for the interior gable walls	\$ 2,515.05	
43	\$ 8.40		10" stack double round flat top & bottom log beam to support floor joist	\$ 361.20	
76	\$ 9.60		2-Log cross ties, 9" top diameter	\$ 729.60	
456	\$ 6.40		Optional log floor joist, flat one side 10" top diameter	\$ 2,918.40	
50	\$ 3.68		8' post, 8" top diameter	\$ 184.00	
64	\$ 4.80		Log ridge beam	\$ 307.20	
5,018	\$ 0.50		1/4" x 1/4" bead of conceal log caulk inside and out for the basic package	\$ 2,508.90	
5,018	\$ 0.60		Foam Gasketing and Fastwing Log Screws	\$ 3,010.68	
17		\$172.50	Log stairs (\$172.50 per tread includes split log treads and 2 choices of log stringers)	\$ 2,932.50	
8		\$ 24.38	*Cedar log post 6" diameter x 48" high with pre notching and drilling (figure one post per 8' section of rail plus one for the end)	\$ 195.04	
20	\$ 18.00		*Pre-assembled northern white cedar log railings for horizontal areas.	\$ 360.00	
16	\$ 21.75		*Pre-assembled northern white cedar log railings for stairs.	\$ 348.00	
			*Total for interior log railings: \$694.40		
			*For the exterior railings you may need 7-7' sections and 5-48" posts	\$ 949.02	
64	\$ 140.00		64FT log porch to cover an 8ft wide deck with log posts 8ft on center and a single log beam with log rafters 4ft on center and covered with 2x8 tongue and groove.	\$ 8,960.00	
1,690	\$ 1.78 / sqft		\$1.78 sq.ft. for 2" x 8" Tongue and groove pine floor for the loft	\$ 3,007.49	
			Total for all options	\$ 29,287.08	
This is a ballpark estimate for the size listed, * log railings are not plan specific, for an exact price please submit a full set of plans or a detailed list of materials. We would be happy to help please give us a call.					
Shipping is estimated for one load in central Wisconsin area, and includes a piggy back fork lift and unloading the truck. If you need a quote for another area please call. Note: your order may require more loads.					
All orders require a deposit of 50%. The balance will be due before shipment. Final payments payable by cashers check unless paid in advance. Deposits are non-refundable. This is an estimate for log materials only and does not include: labor, foundation, sub-floor, roof, interior walls, windows, doors, etc.				Sub-Total	\$ 20,065.05
				5.5% WI Tax	\$ 1,103.58
				Shipping Estimate	\$ 450.00
				Total Due	\$ 21,618.63

Basic log package before tax and shipping	Sub-total	\$ 20,065.05
Total for all options	Options total	\$ 29,287.08
Complete log package estimate before tax and shipping	Total	\$ 49,352.13

Note: 5.5% Sales Tax is only for Wisconsin Residents

Enter dimension information here


Dimensions		
ENTER	Width	36
ENTER	Length	64
ENTER	Additional full log walls	60
ENTER	Wall Height	10
# courses	Main sqft total	2,304
15	Loft sqft total	1,536
# corners	Total sqft	3,840
10	sub-total	\$ 20,065.05
wall footage	option total	\$ 29,287.08
260	total total	\$ 49,352.13
	nat. tails	\$ 2,700.00
	total w/tails	\$ 52,052.13



Inside view with wane on the corners



Matching 3" x 8" log siding

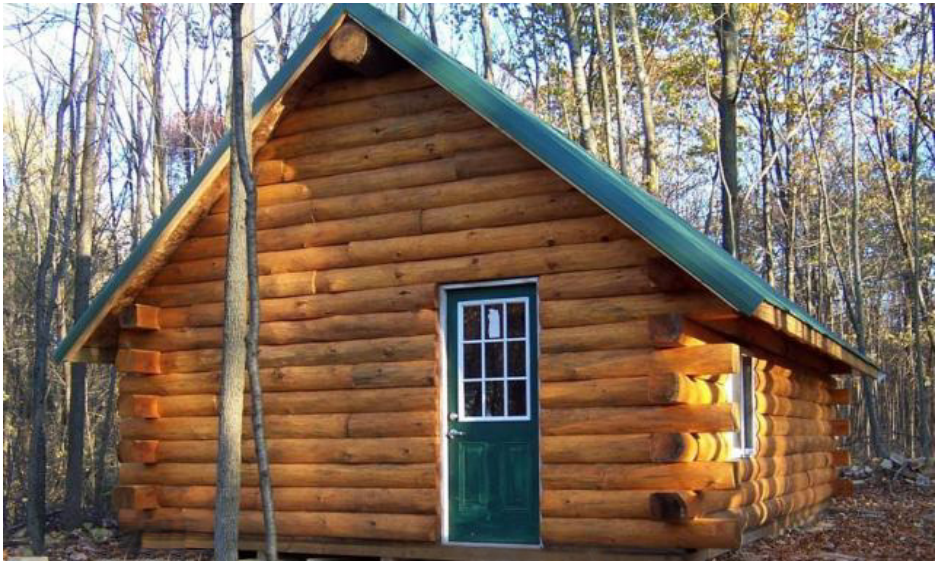

Natural hand-peeled D-Logs
